


WEEKLY PROGRESS REPORT

Week - 14

From 30-Jan-26 ~ 5-Feb-26

Location of the 17 Institutes selected for the Project

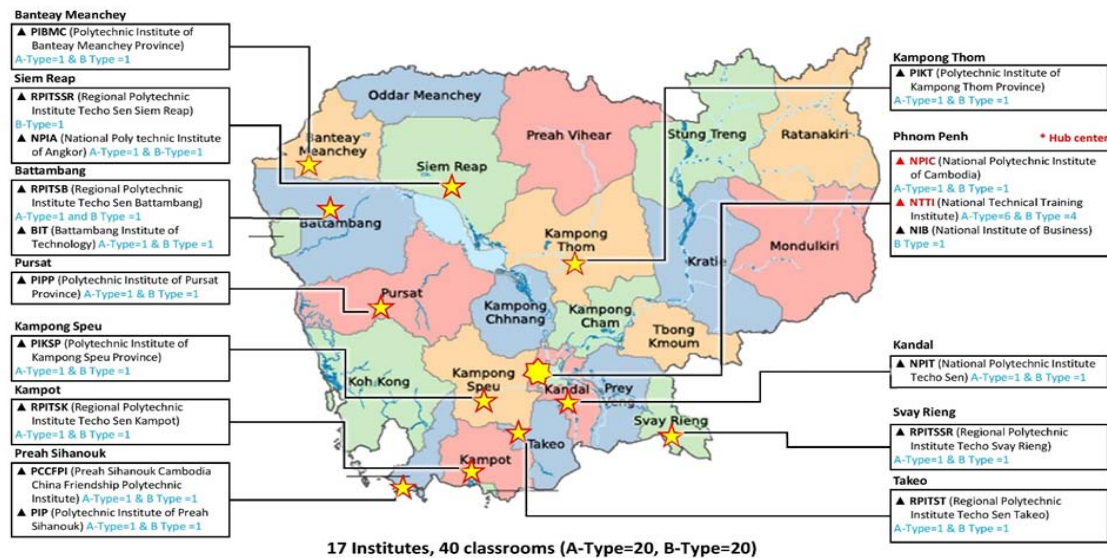

Renovation Works of The Project for Building Capacity and Establishing Enabling Environment in ICT Majors of TVET in Cambodia

Employer : KOICA Cambodia Office

Contractor : Cambodian Advanced Construction Project Management (CACPM)Co., Ltd

LETTER FOR WEEKLY PROGRESS REPORT No.14

Ref. No. : ICT-CPM-LETTER-14

Date : 6-Feb-26

To : **KOICA Cambodia Office**
12th Floor, Exchange Square, Building Nos19. And 20, Street 106, Village 2,
Sangkat Wat Phnom, Khan Daun Penh, Phnom Penh, Cambodia

Att. : **Mr. Chang Woo Jin / CM of Korea International Cooperation Agency**

CC : **Ms. Kim Sujin / Deputy Country Director of KOICA**

: **Mr. Sao Dona / Senior Specialist of KOICA**

: **Mr. Hourn Kimhour / Assistant CM of KOICA**

Dear Sir,

We are pleased to submit Weekly Progress Report No-14 from 30-Jan-26 to 5-Feb-26 for Renovation Works of The Project for Building Capacity and Establishing Enabling Environment in ICT Majors of TVET in Cambodia.

Sincerely Yours,



Mr. Milko Orecchia | Project Manager
Cambodian Advanced Construction Project Management (CACPM)

8th Floor, K1 Tower, No.148, Mao Tse Toung Boulevard (245), Sangkat Toul Tumpong II,
Khan Chamkarmorn, Phnom Penh, Cambodia

T +855 (0) 23 964 417~8 | M +855 (0) 11 693 415
o.milko@cambodiacpm.com
www.cambodiacpm.com

TABLE OF CONTENTS*

1. INTRODUCTION
2. OVERALL PROGRESS OF THIS WEEK AND NEXT WEEK
3. ACTIVITIES OF WORK DONE / NEXT WEEK PLAN
4. QA/QC STATUS
 - 4.1 Non-Conformity Report (NCR)
 - 4.2 Corrective Action Request (CAR)
 - 4.3 Safety Corrective Action Request (SCAR)
 - 4.4 PM Site Instruction (SI)
 - 4.5 Client Site Instruction (SI)
 - 4.6 Inspection Request (IR)
 - 4.7 Material for Approval (MFA)
 - 4.8 Request for Information (RFI)
 - 4.9 Request for Approval (RFA)
 - 4.10 Field Change Request (FCR)
 - 4.11 Variation Order (VO)
 - 4.12 Transmittal (TR)
5. HEALTH, SAFETY, ENVIRONMENTAL & SECURITY (HSES)
 - 5.1 HSES Training / Introduction / Toolbox Meeting
 - 5.2 HSES Inspection / Audit / Heavy Equipment / Hand&Power Tool Checklist
 - 5.3 Permit to Work
 - 5.4 First Aid / Accident / Incident / Near Miss / Fatalities (if Any)
 - 5.5 Other HSES Activities Concerns
 - 5.6 HSES Photo Reference
6. RESOURCES STATUS
 - 6.1 Manpower Status
 - 6.2 Material Delivery Status
 - 6.3 Machinery / Equipment Status
7. SITE ACTIVITY PHOTOS
8. CONSTRUCTION ISSUE
9. MASTER SCHEDULE

1. INTRODUCTION

Project Overview

This project aims to strengthen the ICT education capacity of TVET and to improve the ICT education environment of the existing TVET institutes in Cambodia. ICT Labs will be established and furnished for the TVET.

For this Project, 17 institutes have been selected by KOICA and MLVT Cambodia; 2 as Hub Centers and 15 as Leading institutes. Each institute has secured existing classrooms to be renovated into an ICT Lab with the capacity of 30 persons (A-Type: 30 sets of computers with 15 desks / B-Type (or H-Type): 30 sets of computers with 15 desks + 2 working tables).


Remodelling Work to renovate the existing classrooms into ICT Labs for a better ICT education environment is one of the Project scopes. This bidding is to select a Contractor to conduct the Remodelling Work.

Design & Construction

Cambodian Advanced Construction Project Management Co., Ltd (CACPM) is a design, engineering and construction project management company with core services portfolio including Architecture, Urban planning, Civil, Structure, MEP Engineering, Cost Management, Property Management, Owner-team consultation Turnkey Projects and Feasibility Study.

CACPM was appointed as Contractor by client for this project to carry out the scope of works as follows:

- Architectural Work
- Electrical Work
- Miscellaneous and Common Work

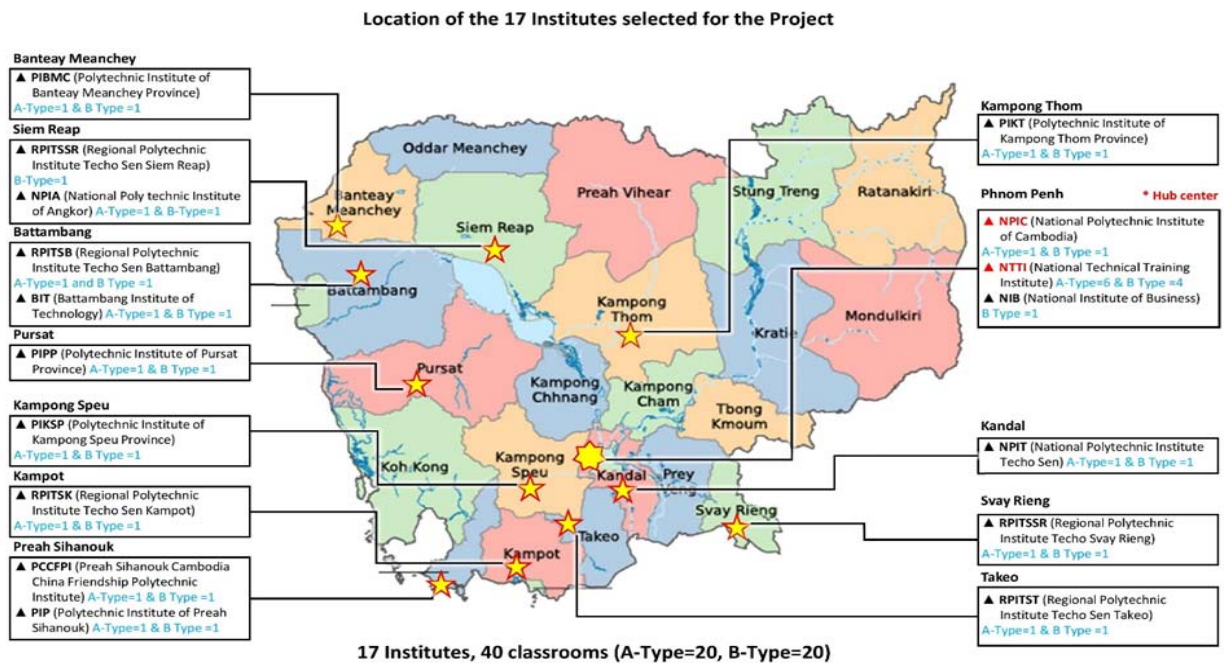

2. OVERALL PROGRESS OF THIS WEEK AND NEXT WEEK

No	Scope of Works	% Up to Previous Week	% This Week	% Up to This Week	% Remaining	% Next Week Plan	% Up Next Week Plan
I	INVESTIGATION PHASE	100.0%	0.0%	100.0%	0.0%	0.0%	100.0%
1	Site survey	100.0%	0.0%	100.0%	0.0%	0.0%	100.0%
2	Drawing (Existing & Construction)	100.0%	0.0%	100.0%	0.0%	0.0%	100.0%
3	BoQ	100.0%	0.0%	100.0%	0.0%	0.0%	100.0%
II	CONSTRUCTION PHASE	1.4%	3.0%	4.4%	95.6%	6.4%	10.8%
1	Battambang Province	0.0%	0.0%	0.0%	100.0%	0.0%	0.0%
2	Banteay Meanchey Province	9.6%	16.1%	25.7%	74.3%	29.7%	55.4%
3	Pursat Province Province	0.0%	0.0%	0.0%	100.0%	0.0%	0.0%
4	Kampong Thom Province	0.2%	26.4%	26.7%	73.3%	19.0%	45.6%
5	Siem Reap Province	0.0%	0.0%	0.0%	100.0%	3.8%	3.8%
6	Phnom Penh	1.6%	0.8%	2.3%	97.7%	4.0%	6.4%
7	Kandal Province	0.0%	0.0%	0.0%	100.0%	0.0%	0.0%
8	Takeo Province	0.0%	0.0%	0.0%	100.0%	0.0%	0.0%
9	Svay Rieng Province	0.0%	0.0%	0.0%	100.0%	0.0%	0.0%
10	Preah Sihanouk	2.1%	8.9%	11.0%	89.0%	22.1%	33.1%
11	Kampot Province	0.0%	0.0%	0.0%	100.0%	0.0%	0.0%
12	Kampong Speu Province	4.7%	5.3%	10.0%	90.0%	11.7%	21.7%

3. ACTIVITIES OF WORK DONE / NEXT WEEK PLAN

Activities of Work Done		Next Week Plan	
I. Investigation Phase	100.0%	I. Investigation Phase	0.0%
1. Site survey	100.0%	1. Site survey	0.0%
2. Drawing (Existing & Construction)	100.0%	2. Drawing (Existing & Construction)	0.0%
3. BoQ	100.0%	3. BoQ	0.0%
II. Construction Phase	4.4%	II. Construction Phase	6.4%
1. Battambang Province	0.0%	1. Battambang Province	0.0%
1.1. Battambang Institute of Technology (BIT)	0.0%	1.1. Battambang Institute of Technology (BIT)	0.0%
1.1.1. Room A-Type	0.0%	1.1.1. Room A-Type	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
1.1.2. Room B-Type	0.0%	1.1.2. Room B-Type	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
1.2. Regional Polytechnic Institute Techo Sen Battambang (RPITSB)	0.0%	1.2. Regional Polytechnic Institute Techo Sen Battambang (RPITSB)	0.0%
1.2.1. Room A-Type	0.0%	1.2.1. Room A-Type	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
1.2.2. Room B-Type	0.0%	1.2.2. Room B-Type	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
2. Banteay Meanchey Province	25.7%	2. Banteay Meanchey Province	29.7%
2.1. Polytechnic Institute of Banteay Meanchey Province (PIBMC)	25.7%	2.1. Polytechnic Institute of Banteay Meanchey Province (PIBMC)	29.7%
2.1.1. Room A-Type	22.0%	2.1.1. Room A-Type	26.3%
- Architectural work	0.0%	- Architectural work	10.1%
- Electrical Works	42.3%	- Electrical Works	43.6%
- Miscellaneous and Common work	19.2%	- Miscellaneous and Common work	9.6%
2.1.2. Room B-Type	29.0%	2.1.2. Room B-Type	32.8%
- Architectural work	0.0%	- Architectural work	14.4%
- Electrical Works	42.2%	- Electrical Works	43.2%
- Miscellaneous and Common work	21.3%	- Miscellaneous and Common work	10.7%
3. Pursat Province Province	0.0%	3. Pursat Province Province	0.0%
3.1. Polytechnic Institute of Pursat Province (PIPP)	0.0%	3.1. Polytechnic Institute of Pursat Province (PIPP)	0.0%
3.1.1. Room A-Type	0.0%	3.1.1. Room A-Type	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
3.1.2. Room B-Type	0.0%	3.1.2. Room B-Type	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
4. Kampong Thom Province	26.7%	4. Kampong Thom Province	19.0%
4.1. Polytechnic Institute of Kampong Thom Province (PIKT)	26.7%	4.1. Polytechnic Institute of Kampong Thom Province (PIKT)	19.0%
4.1.1. Room A-Type	23.4%	4.1.1. Room A-Type	17.5%
- Architectural work	2.0%	- Architectural work	2.0%
- Electrical Works	42.4%	- Electrical Works	31.5%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
4.1.2. Room B-Type	29.2%	4.1.2. Room B-Type	20.1%
- Architectural work	9.4%	- Architectural work	3.8%
- Electrical Works	43.1%	- Electrical Works	30.7%

3. ACTIVITIES OF WORK DONE / NEXT WEEK PLAN

Activities of Work Done		Next Week Plan	
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
5. Siem Reap Province	0.0%	5. Siem Reap Province	3.8%
5.1. National Polytechnic Institute of Angkor (NPIA)	0.0%	5.1. National Polytechnic Institute of Angkor (NPIA)	6.4%
5.1.1. Room A-Type	0.0%	5.1.1. Room A-Type	6.4%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	14.2%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
5.1.2. Room B-Type	0.0%	5.1.2. Room B-Type	6.4%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	14.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
5.2. Regional Polytechnic Institute Techo Sen Siem Reap (RPITSSR)	0.0%	5.2. Regional Polytechnic Institute Techo Sen Siem Reap (RPITSSR)	0.0%
5.2.1. Room B-Type	0.0%	5.2.1. Room B-Type	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
6. Phnom Penh	2.3%	6. Phnom Penh	4.0%
6.1. National Polytechnic Institute of Cambodia (NPIC)	0.0%	6.1. National Polytechnic Institute of Cambodia (NPIC)	0.0%
6.1.1. Room A-Type	0.0%	6.1.1. Room A-Type	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
6.1.2. Room B-Type	0.0%	6.1.2. Room B-Type	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
6.2. National Technical Training Institute (NTTI)	2.2%	6.2. National Technical Training Institute (NTTI)	2.9%
6.2.1. Room A-Type-1	0.0%	6.2.1. Room A-Type-1	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
6.2.2. Room A-Type-2	0.0%	6.2.2. Room A-Type-2	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
6.2.3. Room A-Type-3	0.0%	6.2.3. Room A-Type-3	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
6.2.4. Room A-Type-4	0.0%	6.2.4. Room A-Type-4	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
6.2.5. Room A-Type-5	7.4%	6.2.5. Room A-Type-5	9.5%
- Architectural work	8.2%	- Architectural work	11.2%
- Electrical Works	7.2%	- Electrical Works	9.0%
- Miscellaneous and Common work	2.8%	- Miscellaneous and Common work	0.0%
6.2.6. Room A-Type-6	7.4%	6.2.6. Room A-Type-6	9.5%
- Architectural work	8.2%	- Architectural work	11.1%
- Electrical Works	7.2%	- Electrical Works	9.0%
- Miscellaneous and Common work	2.8%	- Miscellaneous and Common work	0.0%
6.2.7. Room B-Type-1	0.0%	6.2.7. Room B-Type-1	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%

3. ACTIVITIES OF WORK DONE / NEXT WEEK PLAN

Activities of Work Done		Next Week Plan	
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
6.2.8. Room B-Type-2	8.6%	6.2.8. Room B-Type-2	11.7%
- Architectural work	10.2%	- Architectural work	15.0%
- Electrical Works	7.2%	- Electrical Works	9.0%
- Miscellaneous and Common work	3.3%	- Miscellaneous and Common work	0.0%
6.2.9. Room B-Type-3	0.0%	6.2.9. Room B-Type-3	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
6.2.10. Room B-Type-4	0.0%	6.2.10. Room B-Type-4	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
6.3. National Institute of Business (NIB)	7.1%	6.3. National Institute of Business (NIB)	20.4%
6.3.1. Room B-Type	7.1%	6.3.1. Room B-Type	20.4%
- Architectural work	7.8%	- Architectural work	21.8%
- Electrical Works	6.7%	- Electrical Works	20.5%
- Miscellaneous and Common work	3.0%	- Miscellaneous and Common work	7.0%
7. Kandal Province	0.0%	7. Kandal Province	0.0%
7.1. National Polytechnic Institute of Techo Sen (NPIT)	0.0%	7.1. National Polytechnic Institute of Techo Sen (NPIT)	0.0%
7.1.1. Room A-Type	0.0%	7.1.1. Room A-Type	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
7.1.2. Room B-Type	0.0%	7.1.2. Room B-Type	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
8. Takeo Province	0.0%	8. Takeo Province	0.0%
8.1. Regional Polytechnic Institute Techo Sen Takeo (RPITST)	0.0%	8.1. Regional Polytechnic Institute Techo Sen Takeo (RPITST)	0.0%
8.1.1. Room A-Type	0.0%	8.1.1. Room A-Type	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
8.1.2. Room B-Type	0.0%	8.1.2. Room B-Type	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
9. Svay Rieng Province	0.0%	9. Svay Rieng Province	0.0%
9.1. Regional Polytechnic Institute Techo Sen Svay Rieng (RPITSSR)	0.0%	9.1. Regional Polytechnic Institute Techo Sen Svay Rieng (RPITSSR)	0.0%
9.1.1. Room A-Type	0.0%	9.1.1. Room A-Type	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
9.1.2. Room B-Type	0.0%	9.1.2. Room B-Type	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
10. Preah Sihanouk	11.0%	10. Preah Sihanouk	22.1%
10.1. Preah Sihanouk Cambodia China Friendship Polytechnic Institute (PCCFPI)	14.0%	10.1. Preah Sihanouk Cambodia China Friendship Polytechnic Institute (PCCFPI)	19.6%
10.1.1. Room A-Type	13.4%	10.1.1. Room A-Type	12.9%
- Architectural work	9.8%	- Architectural work	5.1%
- Electrical Works	20.3%	- Electrical Works	24.4%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%

3. ACTIVITIES OF WORK DONE / NEXT WEEK PLAN

Activities of Work Done		Next Week Plan	
10.1.2. Room B-Type	 14.5%	10.1.2. Room B-Type	 24.2%
- Architectural work	 12.1%	- Architectural work	 16.4%
- Electrical Works	 20.2%	- Electrical Works	 37.9%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
10.2. Polytechnic Institute of Preah Sihanouk (PIP)	 8.2%	10.2. Polytechnic Institute of Preah Sihanouk (PIP)	 24.3%
10.2.1. Room A-Type	 7.1%	10.2.1. Room A-Type	 23.4%
- Architectural work	 13.0%	- Architectural work	 6.7%
- Electrical Works	0.0%	- Electrical Works	 50.0%
- Miscellaneous and Common work	 5.1%	- Miscellaneous and Common work	 0.6%
10.2.2. Room B-Type	 9.0%	10.2.2. Room B-Type	 24.9%
- Architectural work	 16.8%	- Architectural work	 10.0%
- Electrical Works	0.0%	- Electrical Works	 50.0%
- Miscellaneous and Common work	 5.7%	- Miscellaneous and Common work	 0.6%
11. Kampot Province	0.0%	11. Kampot Province	0.0%
11.1. Regional Polytechnic Institute Techo Sen Kampot (RPITSK)	0.0%	11.1. Regional Polytechnic Institute Techo Sen Kampot (RPITSK)	0.0%
11.1.1. Room A-Type	0.0%	11.1.1. Room A-Type	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
11.1.2. Room B-Type	0.0%	11.1.2. Room B-Type	0.0%
- Architectural work	0.0%	- Architectural work	0.0%
- Electrical Works	0.0%	- Electrical Works	0.0%
- Miscellaneous and Common work	0.0%	- Miscellaneous and Common work	0.0%
12. Kampong Speu Province	10.0%	12. Kampong Speu Province	11.7%
12.1. Polytechnic Institute of Kampong Speu Province (PIKSP)	 10.0%	12.1. Polytechnic Institute of Kampong Speu Province (PIKSP)	 11.7%
12.1.1. Room A-Type	 11.7%	12.1.1. Room A-Type	 10.6%
- Architectural work	 8.7%	- Architectural work	 12.9%
- Electrical Works	 18.9%	- Electrical Works	 10.0%
- Miscellaneous and Common work	 3.7%	- Miscellaneous and Common work	 1.2%
12.1.2. Room B-Type	 8.7%	12.1.2. Room B-Type	 12.4%
- Architectural work	 2.2%	- Architectural work	 17.1%
- Electrical Works	 19.2%	- Electrical Works	 10.0%
- Miscellaneous and Common work	 3.6%	- Miscellaneous and Common work	 2.2%

4. QA/QC STATUS

4.1 Non-Conformity Report (NCR)

Code	Description	Status	Date Responded
<u>Comments</u>			

4.2 Corrective Action Request (CAR)

Code	Description	Status	Date Responded
<u>Comments</u>			

4.3 Safety Corrective Action Request (SCAR)

Code	Description	Status	Date Responded
<u>Comments</u>			

4.4 PM Site Instruction (SI)

Code	Description	Status	Date Responded
<u>Comments</u>			

4.5 Client Site Instruction (SI)

Code	Description	Issued By	Issued Date

4. QA/QC STATUS

<u>Comments</u>			

4.6 Inspection Request (IR)

Code	Description	Received Date	Inspection Date
<u>Comments</u>			

4.7 Material for Approval (MFA)

Code	Description	Status	Date Responded
ICT-CPM-MFA-AR-001-R0	Material List For Architectural Works	Approved with condition	13-Jan-2026
ICT-CPM-MFA-ME-001-R0	Material List For Electrical and Mechanical Works	Approved with condition	13-Jan-2026
ICT-CPM-MFA-AR-001-R0	Material List For Architectural Works	Resubmit	
ICT-CPM-MFA-ME-001-R0	Material List For Electrical and Mechanical Works	Resubmit	
ICT-CPM-MFA-AR-001-R2	Material List For Architectural Works	Approved	23-Jan-2026
ICT-CPM-MFA-ME-001-R2	Material List For Electrical and Mechanical Works	Approved	23-Jan-2026
ICT-CPM-MFA-AR-001-R3	Material List For Architectural Works		
<u>Comments</u>			

4.8 Request for Information (RFI)

Code	Description	Status	Date Responded
CKR-CPM-RFI-001	Request for information regarding Roof Leakage NTTI Institute	Respond	26-Dec-2025
CKR-CPM-RFI-002	Request for Authorization to Begin Work NPIT (Kandal) - PIKSP (Kampon Speu) - RPITSSR (Seam Reap)	Respond	26-Dec-2025
<u>Comments</u>			

4.9 Request for Approval (RFA)

Code	Description	Status	Date Responded
ICT-CPM-RFA-001-R0	Scope of work form sample		
ICT-CPM-RFA-002-R0	Site Investigation Results for all 17 Institutes		
ICT-CPM-RFA-003-R0	Scope of work form sample for all 17 Institutes		
ICT-CPM-RFA-004-R0	Submission Final Investigation Report		
ICT-CPM-RFA-004-R1	Submission Final Investigation Report		

4. QA/QC STATUS

ICT-CPM-RFA-004-R2	Submission Revised Scope of Work, Detailed Architectural Design Drawings, Detailed MEP Design Drawings		
ICT-CPM-RFA-004-R3	Submission Revised Electrical Drawings		
ICT-CPM-RFA-005-R0	Submission Classrooms Signboard Proposal	Approved with condition	4-Feb-2026
ICT-CPM-RFA-005-R1	Submission Revised Classrooms Signboard Proposal		
<u>Comments</u>			

4.10 Field Change Request (FCR)

Code	Description	Status	Date Responded
<u>Comments</u>			

4.11 Variation Order (VO)

Code	Description	Status	Date Responded
<u>Comments</u>			

4.12 Transmittal (TR)

Code	Description	Status	Date Responded
<u>Comments</u>			

5. HEALTH, SAFETY, ENVIRONMENTAL & SECURITY (HSES)

5.1 HSES Training / Introduction / Toolbox Meeting

Type of Training	Date	Venue	Trainer	Attendee	Remarks
HSE induction training course	27-Jan-26	PIBMC	Vetou	2	Banteay Meanchey
HSE induction training course	31-Jan-26	PIBMC	Vetou	1	
HSE induction training course	4-Feb-26	PIBMC	Vetou	1	
HSE induction training course	27-Jan-26	PIKT	Boribo	2	Kampong Thom
HSE induction training course	28-Jan-26	PIKT	Boribo	2	
HSE induction training course	31-Jan-26	PIKT	Boribo	1	
HSE induction training course	23-Jan-26	NTTI	Lyheang	8	Phnom Penh
HSE induction training course	26-Jan-26	NTTI	Lyheang	8	
HSE induction training course	23-Jan-26	NIB	Ramon	3	
HSE induction training course	27-Jan-26	NIB	Ramon	3	
HSE induction training course	29-Jan-26	PIP	Sopheak	8	Preah Sihanouk
HSE induction training course	2-Feb-26	PCCFPI	Sopheak	7	
HSE induction training course	23-Jan-26	PIKSP	Phearum	6	Kampong Speu

5.2 HSES Inspection / Audit / Heavy Equipment / Hand&Power Tool Checklist

Type of Inspection	Date	Inspector	Remarks
Tool and equipment inspection	31-Jan-26	Vetou	Banteay Meanchey
Tool and equipment inspection	28-Jan-26	Boribo	Kampong Thom
Tool and equipment inspection	30-Jan-26	Ramon	Phnom Penh
Tool and equipment inspection	4-Feb-26	Lyheang	
Tool and equipment inspection	29-Jan-26	Sopheak	Preah Sihanouk
Tool and equipment inspection	2-Feb-26	Sopheak	
Tool and equipment inspection	27-Jan-26	Phearum	Kampong Speu

5.3 Permit to Work

Type of Permit	Start Date	End Date	Inspector	Approver	Remarks

5.4 First Aid / Accident / Incident / Near Miss / Fatalities (if Any)


.....

5.5 Other HSES Activities Concerns

.....

5. HEALTH, SAFETY, ENVIRONMENTAL & SECURITY (HSES)

5.6 HSES Photo Reference

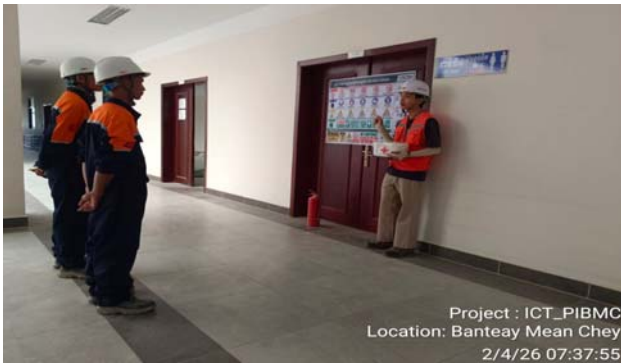HSE Toolbox Meeting	
 Project : ICT_PIBMC Location: Banteay Mean Chey 2/4/26 07:36:51	 Project : ICT_PIBMC Location: Banteay Mean Chey 2/4/26 07:37:55
PIBMC: Toolbox Meeting	PIBMC: Toolbox Meeting
 Project: ICT Location: PIKT Kampong Thom 5 Feb 2026 at 06:54:19	 Project: ICT Location: PIKT Kampong Thom 5 Feb 2026 at 06:54:33
PIKT: Toolbox Meeting	PIKT: Toolbox Meeting
 Project: ICT Location: PIKT Kampong Thom 4 Feb 2026 at 07:01:25	 Project: ICT Location: PIKT Kampong Thom 4 Feb 2026 at 07:01:37
PIKT: Toolbox Meeting	PIKT: Toolbox Meeting
 Feb 3, 2026 at 07:16:52 +11.567965,+104.877010 ±3.44m 263° W Phnom Penh Cambodia កម្ពុជា Altitude: 22.3meter Speed: 0.0km/h	 Feb 3, 2026 at 13:02:35 +11.567986,+104.877055 ±2.96m 87° E Phnom Penh Cambodia កម្ពុជា Altitude: 38.7meter Speed: 0.0km/h
NTTI: Toolbox Meeting	NTTI: Toolbox Meeting

5. HEALTH, SAFETY, ENVIRONMENTAL & SECURITY (HSES)



NIB: Toolbox Meeting



NIB: Toolbox Meeting



NIB: Toolbox Meeting



NIB: Toolbox Meeting



PIP: Toolbox Meeting



PCCFPI: Toolbox Meeting



PCCFPI: Toolbox Meeting



PCCFPI: Toolbox Meeting

5. HEALTH, SAFETY, ENVIRONMENTAL & SECURITY (HSES)

	
PIKSP: Toolbox Meeting	PIKSP: Toolbox Meeting
HSE Activity Photo	
	
PIBMC: First aid and fire extinguisher	PIBMC: Health and safety sign
	
PIBMC: Worker wearing PPE	PIBMC: HSE activity
	
PIKT: HSE activities	PIKT: HSE activities

5. HEALTH, SAFETY, ENVIRONMENTAL & SECURITY (HSES)



PIKT: HSE activities



PIKT: HSE activities



NIB: HSE training



NIB: HSE training



NIB: HSE training



NIB: HSE training



PCCFPI: HSE training



PCCFPI: HSE training

6. RESOURCES STATUS

6.1 Manpower Status

Description	Feb-26							Previous Week	This Week	Up to This Week
	Fri 30	Sat 31	Sun 1	Mon 2	Tue 3	Wed 4	Thu 5			
I. Site Management Team										
1. Project Manager	0	0	0	0	0	0	0	0	0	0
2. Construction Manager	0	0	0	0	0	0	0	0	0	0
3. Architect engineer	0	0	0	0	0	0	0	4	0	4
4. Site Engineer	4	4	1	5	4	5	4	37	27	64
5. MEP Engineer	3	3	0	3	3	3	3	30	18	48
II. Site Working Team (Interior)										
1. Site Engineer	5	5	1	5	5	5	4	26	30	56
2. Skilled Worker	14	16	2	11	10	7	7	63	67	130
3. General Worker	13	15	5	8	6	6	4	77	57	134
III. Site Working Team (MEP)										
1. Site Engineer	0	2	0	1	2	2	2	1	9	10
2. Skilled Worker	3	10	4	10	8	10	9	21	54	75
3. General Worker	2	2	0	2	2	2	2	16	12	28
Total								275	274	549

6.2 Material Delivery Status

Description	Unit	Previous	This Period	Accumulate
Cement	bag	21	50	71
Skim coat	bag	64	0	64
Sand	m3	9	17	26
Brick	pcs	10000	1500	11500
UTP CAT6 cable	roll	0	14	14
PVC pipes	pcs	0	100	100
PVC flexible	roll	0	1	1
uPVC Conduit DN20mm	pcs	0	100	100
PVC Trunking 40x20mm	length	0	15	15
PVC Trunking 50x50mm	length	0	2	2
1Cx1.5mm2 Cu/PVC Black	roll	0	1	1
1Cx1.5mm2 Cu/PVC Red	roll	0	2	2
1Cx2.5mm2 Cu/PVC Black	roll	0	2	2
1Cx2.5mm2 Cu/PVC Red	roll	0	2	2
1Cx2.5mm2 Cu/PVC Green/Yellow	roll	0	2	2
HDMI AOC cable 15m	pcs	0	1	1
UTP cat6 cable 305m/roll	roll	0	13	13
uPVC conduit DN 20mm 2.9m	length	0	28	28
uPVC conduit DN 25mm 2.9m	length	0	20	20
uPVC flexible DN 20mm 50m/roll	roll	0	3	3
uPVC flexible DN 25mm 50m/roll	roll	0	4	4
Electrical back box 85x85x40mm	pcs	0	24	24
Electrical double back box 141x80x50mm	pcs	0	25	25
Electrical Wire 1Cx1.5mm ²	roll	0	7	7
Electrical Wire 1Cx2.5mm ²	roll	0	40	40
Electrical Conduit 20mm	pcs	0	117	117


6. RESOURCES STATUS

Electrical Conduit 25mm	pcs	0	130	130
Flexible Conduit 20mm	roll	0	15	15
Flexible Conduit 25mm	roll	0	7	7


6.3 Machinery / Equipment Status

Description	Feb-26							Previous Week	This Week	Up to This Week
	Fri	Sat	Sun	Mon	Tue	Wed	Thu			
	30	31	1	2	3	4	5			
Scaffolding	2	2	1	2	2	3	3	30	15	45
Hand cutting machine	0	0	0	0	0	0	0	6	0	6
Chipping hammer machine	0	0	0	0	0	0	0	7	0	7
Mobile stair	1	2	2	2	2	3	2	3	14	17
Electric cable	0	0	0	0	0	0	0	4	0	4
Hand drill machine	0	0	0	0	0	0	0	2	0	2
Mixer machine	0	0	0	0	0	0	0	1	0	1
Angle grinder	2	2	2	2	2	2	2	0	14	14
Electric hammer	2	2	2	2	2	2	2	0	14	14
Power cable	1	1	1	1	1	1	1	0	7	7
Electric drill	2	2	1	2	2	4	3	0	16	16
Cut-off machine										
Total								53	80	133

7. SITE ACTIVITY PHOTOS

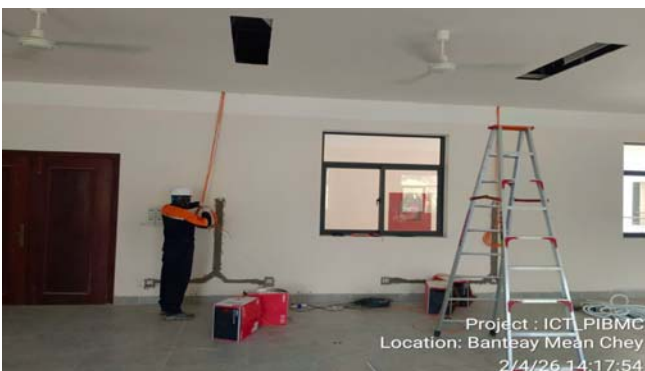SITE ACTIVITY PHOTOS	
Banteay Meanchey (PIBMC)	
 Project : ICT_PIBMC Location: Banteay Mean Chey 2/3/26 08:55:43	 Project : ICT_PIBMC Location: Banteay Mean Chey 2/3/26 08:55:29
Type-A: Installing data cable	Type-A: Installing data cable
 Project : ICT_PIBMC Location: Banteay Mean Chey 2/3/26 08:55:36	 Project : ICT_PIBMC Location: Banteay Mean Chey 2/3/26 14:29:56
Type-A: Installing data cable	Type-A: Installing data cable
 Project : ICT_PIBMC Location: Banteay Mean Chey 2/4/26 08:13:43	 Project : ICT_PIBMC Location: Banteay Mean Chey 2/4/26 14:17:54
Type-B: Installing data cable	Type-B: Installing data cable
 Project : ICT_PIBMC Location: Banteay Mean Chey 2/4/26 08:13:57	 Project : ICT_PIBMC Location: Banteay Mean Chey 2/4/26 14:18:11
Type-B: Installing data cable	Type-B: Installing data cable

7. SITE ACTIVITY PHOTOS

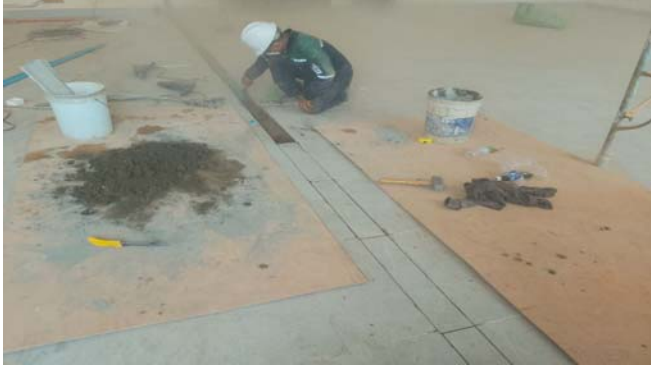SITE ACTIVITY PHOTOS	
Kampong Thom (PIKT)	
 Project: ICT Location: PIKT Kampong Thom 5 Feb 2026 at 07:55:52	 Project: ICT Location: PIKT Kampong Thom 5 Feb 2026 at 07:55:56
Type-A: Wall cutting and re-plaster for socket	Type-A: Wall cutting and re-plaster for socket
 Project: ICT Location: PIKT Kampong Thom 5 Feb 2026 at 08:00:04	 Project: ICT Location: PIKT Kampong Thom 5 Feb 2026 at 10:15:18
Type-B: Wall cutting for socket	Type-B: Wall cutting for socket
 Project: ICT Location: PIKT Kampong Thom 5 Feb 2026 at 08:24:57	 Project: ICT Location: PIKT Kampong Thom 5 Feb 2026 at 08:23:21
Type-B: Lay the floor tile	Type-B: Lay the floor tile
 Project: ICT Location: PIKT Kampong Thom 5 Feb 2026 at 08:24:57	 Project: ICT Location: PIKT Kampong Thom 5 Feb 2026 at 08:23:21
Type-B: Lay the floor tile	Type-B: Lay the floor tile

7. SITE ACTIVITY PHOTOS

SITE ACTIVITY PHOTOS	
Phnom Penh (NTTI)	
	
B-Type-2 Install brick wall for new door and socket box	B-Type-2 Cement fill close louver
	
B-Type-2 Cement fill close louver	A-Type-6 Install brick wall for new door and cement fill close louver
	
A-Type-6 Cement fill close louver	A-Type-5 Cutting wall for build in electrical conduit
	
A-Type-5 Cement fill close louver	A-Type-5 Install brick wall for new door and cement fill close louver

7. SITE ACTIVITY PHOTOS

SITE ACTIVITY PHOTOS	
Phnom Penh (NIB)	
 Network:4 Feb 2026 at 8:28:11 in the morning GMT+7 Phnom Penh, Mean Chey Remark: Project: NIB	 Network:4 Feb 2026 at 8:28:16 in the morning GMT+7 Phnom Penh, Mean Chey Remark: Project: NIB
Type B: Wall marking for power socket and data	Type B:Wall marking for power socket and data
 Network:2 Feb 2026 at 12:52:42 in the afternoon GMT+7 Phnom Penh, Mean Chey Remark: Project: NIB	 Network:2 Feb 2026 at 12:52:47 in the afternoon GMT+7 Phnom Penh, Mean Chey Remark: Project: NIB
Type B: Wall extend	Type B: Wall extend
 Network:30 Jan 2026 at 7:55:56 in the morning GMT+7 Phnom Penh, Mean Chey Remark: Project: NIB	 Network:30 Jan 2026 at 7:55:46 in the morning GMT+7 Phnom Penh, Mean Chey Remark: Project: NIB
Type B: Demolish existing floor tiles	Type B: Demolish existing floor tiles
 DEFINE SPACE Sat, 31 Jan 2026 09:33 វិទ្យាសាស្ត្រសាងសង់សាលាស្រី គម្រោងលេខ 116217, ភូមិមានជ័យ, ខណ្ឌ ទួលគោក, រាជធានី ភ្នំពេញ, 120608 Project: NIB Photo by Timemark	 Network:5 Feb 2026 at 7:49:59 in the morning GMT+7 Phnom Penh, Mean Chey Remark: Project: NIB
Type B: Skim coat painting	Type B: Wall marking for power socket and data

7. SITE ACTIVITY PHOTOS

SITE ACTIVITY PHOTOS	
Preah Sihanouk (PIP)	
	
Type-A: Remove Existing painting	Type-A: Prepare for painting work
	
Type-B: Remove Existing painting	Type-B: Plastering work
	
Type-B: Pre inspection for Ceiling high	Type-B: Skincoat work
	
Type-B: Door painting	Type-B: Prepare for painting

7. SITE ACTIVITY PHOTOS


SITE ACTIVITY PHOTOS	
Preah Sihanouk (PCCFPI)	
	
Type-A: Plastering work	Type-A: MEP work
	
Type-A: MEP work	Type-A: MEP work
	
Type-B: MEP Work	Type-B: Ceiling work
	
Type-B: Ceiling work	Type-B: Plastering work

7. SITE ACTIVITY PHOTOS

SITE ACTIVITY PHOTOS	
Kampong Speu (PIKSP)	
	
Type-B: Block the louver ventilation work	Type-B: Block the louver ventilation work
	
Type-B:Cleaning and repairing joint for existing floor tile	Type-A: Cleaning and repairing joint for existing floor tile
	
Type-B:Remove the existing slid	Type-A: Remove the existing camera
	
Type-A:Remove the existing socket	Type-A: Line marking for lights

8. CONSTRUCTION ISSUE

<u>Construction Issue</u>	
<u>1</u>	
Site Location:	Photo Reference
Problems / Descriptions:	
Action by:	
<u>2</u>	
Site Location:	Photo Reference
Problems / Descriptions:	
Action by:	
<u>3</u>	
Site Location:	Photo Reference
Problems / Descriptions:	
Action by:	
<u>4</u>	
Site Location:	Photo Reference
Problems / Descriptions:	
Action by:	

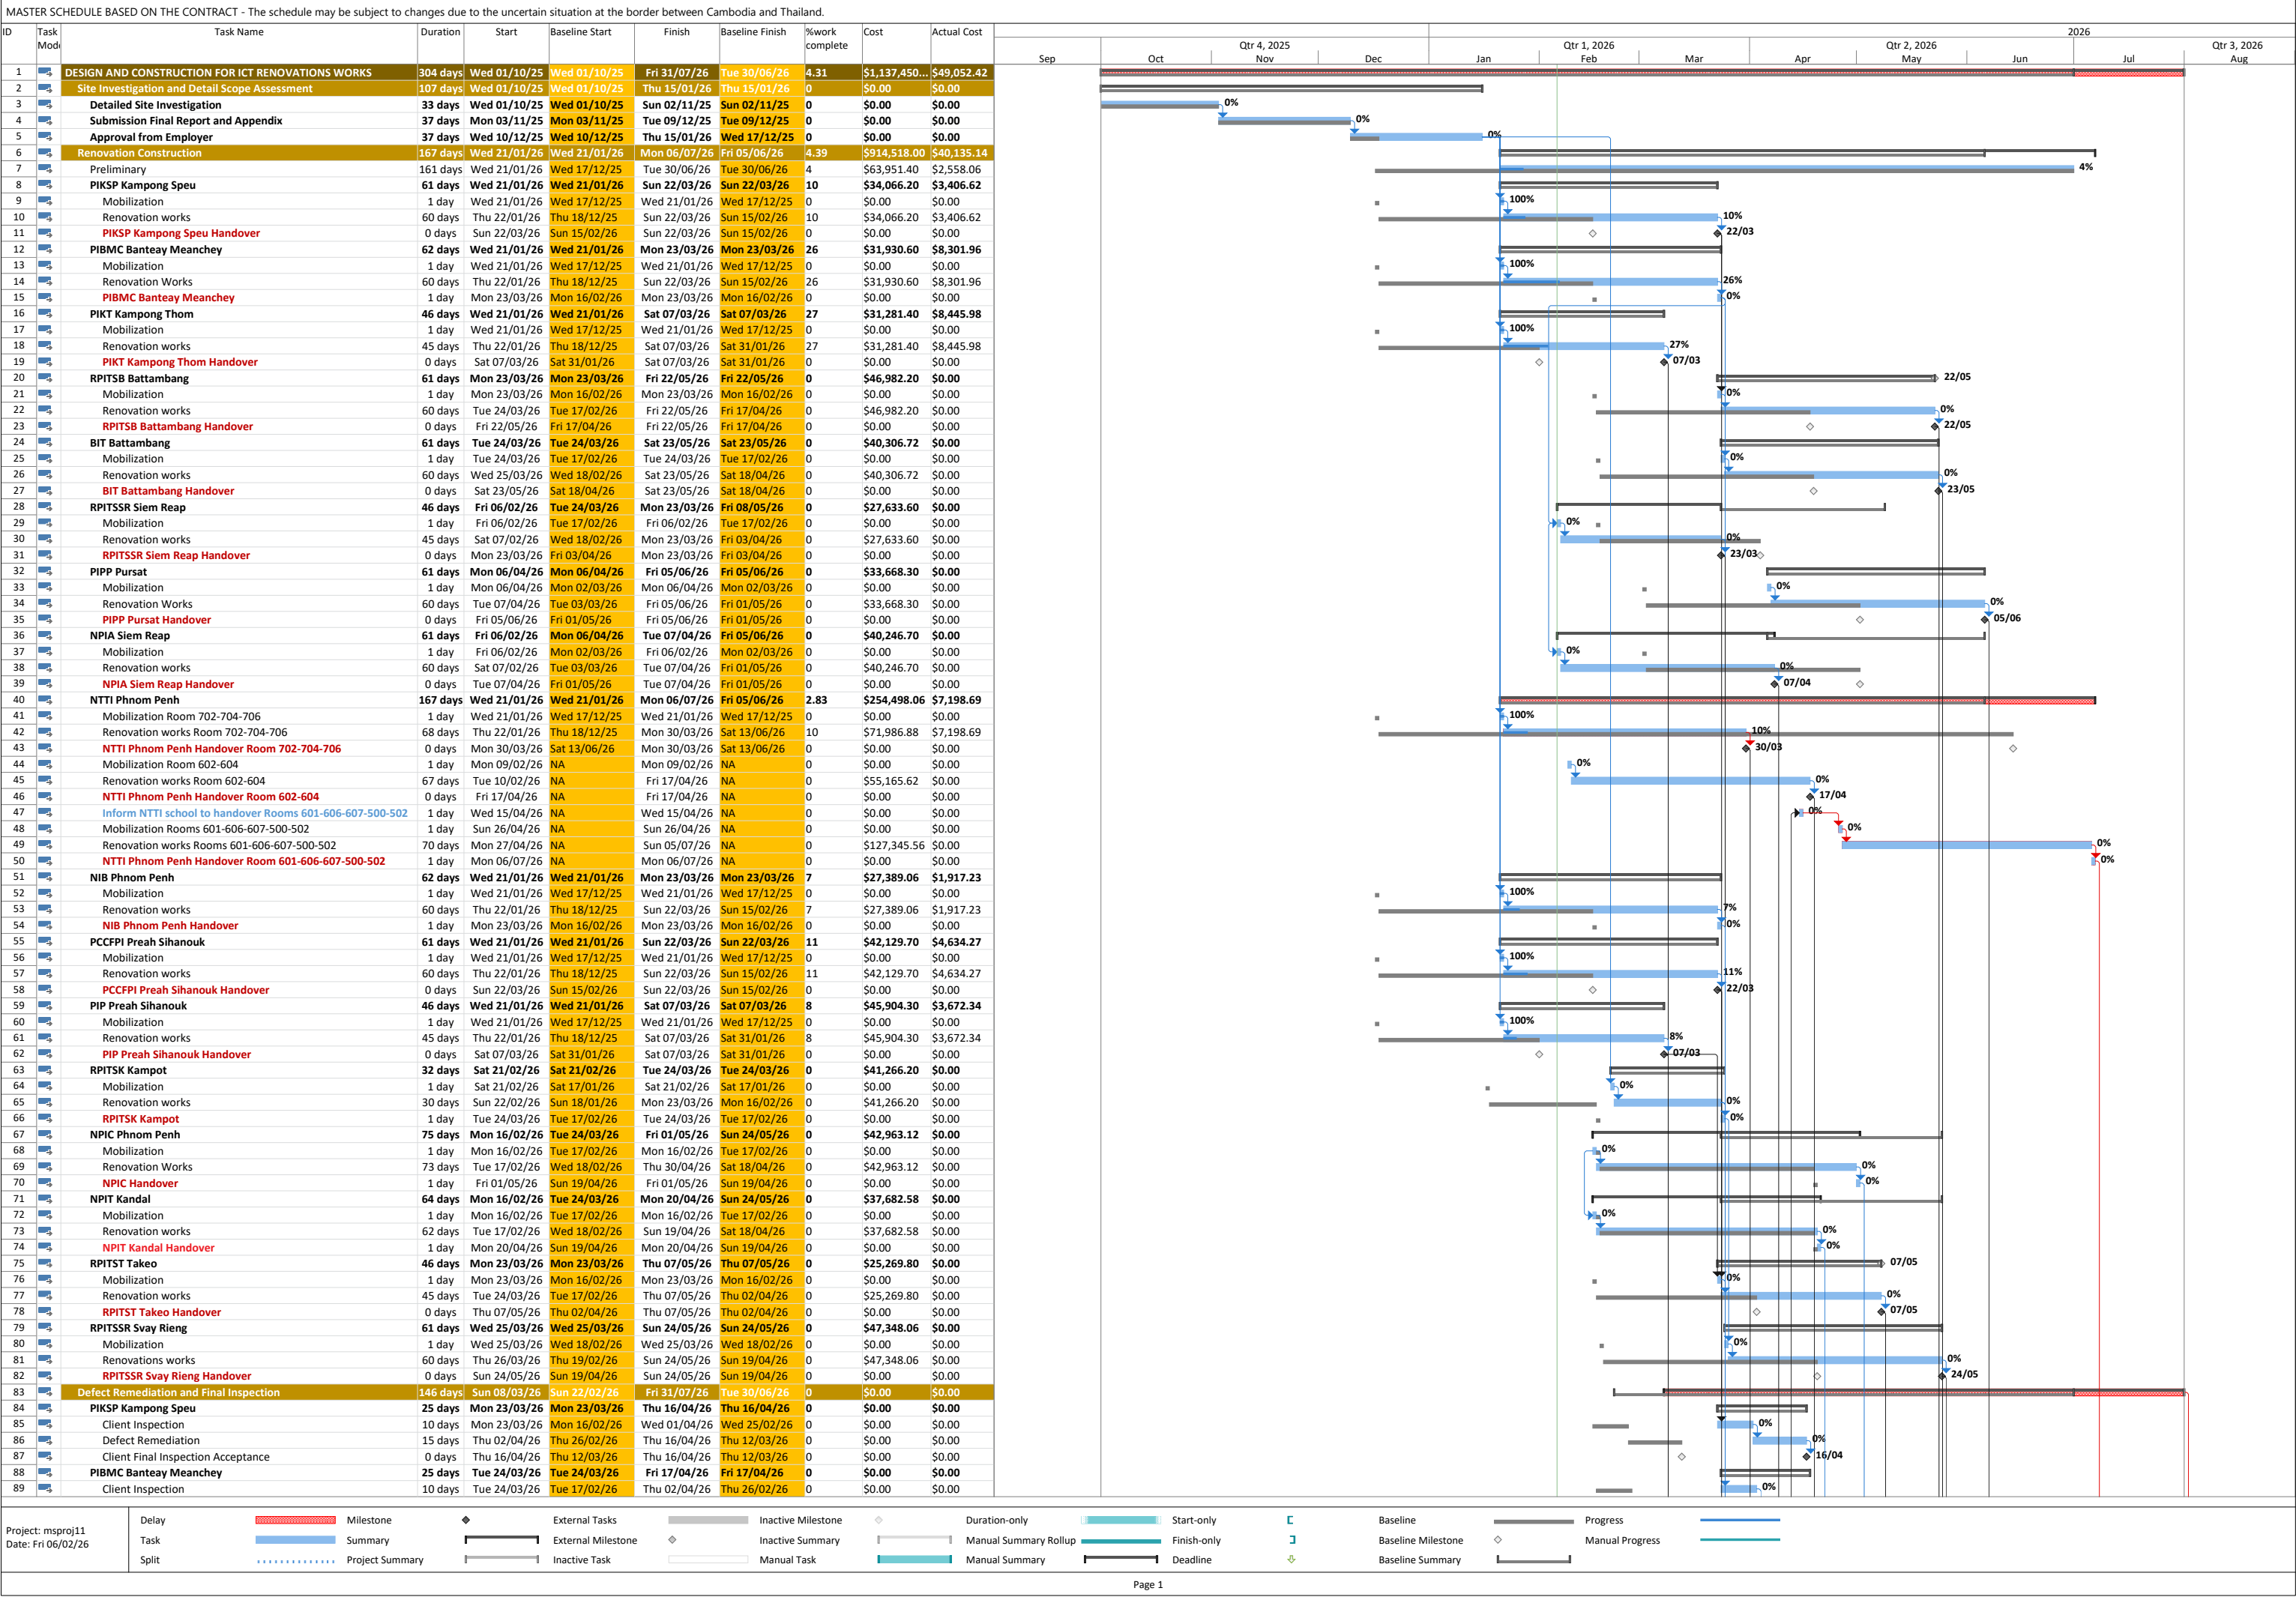

MASTER SCHEDULE BASED ON THE CONTRACT - The schedule may be subject to changes due to the uncertain situation at the border between Cambodia and Thailand.																							
ID	Task Mod	Task Name	Duration	Start	Baseline Start	Finish	Baseline Finish	%work complete	Cost	Actual Cost	Sep	Oct	Qtr 4, 2025	Dec	Jan	Qtr 1, 2026	Mar	Apr	Qtr 2, 2026	2026	Jun	Jul	Qtr 3, 2026
90		Defect Remediation	15 days	Fri 03/04/26	Fri 27/02/26	Fri 17/04/26	Fri 13/03/26	0	\$0.00	\$0.00													
91		Client Final Inspection Acceptance	0 days	Fri 17/04/26	Fri 13/03/26	Fri 17/04/26	Fri 13/03/26	0	\$0.00	\$0.00													
92		PIKT Kampong Thom	25 days	Sun 08/03/26	Sun 08/03/26	Wed 01/04/26	Wed 01/04/26	0	\$0.00	\$0.00													
93		Client Inspection	10 days	Sun 08/03/26	Sun 01/02/26	Tue 17/03/26	Tue 10/02/26	0	\$0.00	\$0.00													
94		Defect Remediation	15 days	Wed 18/03/26	Wed 11/02/26	Wed 01/04/26	Wed 25/02/26	0	\$0.00	\$0.00													
95		Client Final Inspection Acceptance	0 days	Wed 01/04/26	Wed 25/02/26	Wed 01/04/26	Wed 25/02/26	0	\$0.00	\$0.00													
96		RPITSB Battambang	25 days	Sat 23/05/26	Sat 23/05/26	Tue 16/06/26	Tue 16/06/26	0	\$0.00	\$0.00													
97		Client Inspection	10 days	Sat 23/05/26	Sat 18/04/26	Mon 01/06/26	Mon 27/04/26	0	\$0.00	\$0.00													
98		Defect Remediation	15 days	Tue 02/06/26	Tue 28/04/26	Tue 16/06/26	Tue 12/05/26	0	\$0.00	\$0.00													
99		Client Final Inspection Acceptance	0 days	Tue 16/06/26	Tue 12/05/26	Tue 16/06/26	Tue 12/05/26	0	\$0.00	\$0.00													
100		BIT Battambang	25 days	Sun 24/05/26	Sun 24/05/26	Wed 17/06/26	Wed 17/06/26	0	\$0.00	\$0.00													
101		Client Inspection	10 days	Sun 24/05/26	Sun 19/04/26	Tue 02/06/26	Tue 28/04/26	0	\$0.00	\$0.00													
102		Defect Remediation	15 days	Wed 03/06/26	Wed 29/04/26	Wed 17/06/26	Wed 13/05/26	0	\$0.00	\$0.00													
103		Client Final Inspection Acceptance	0 days	Wed 17/06/26	Wed 13/05/26	Wed 17/06/26	Wed 13/05/26	0	\$0.00	\$0.00													
104		RPITSSR Siem Reap	25 days	Tue 24/03/26	Sat 09/05/26	Fri 17/04/26	Tue 02/06/26	0	\$0.00	\$0.00													
105		Client Inspection	10 days	Tue 24/03/26	Sat 04/04/26	Thu 02/04/26	Mon 13/04/26	0	\$0.00	\$0.00													
106		Defect Remediation	15 days	Fri 03/04/26	Tue 14/04/26	Fri 17/04/26	Tue 28/04/26	0	\$0.00	\$0.00													
107		Client Final Inspection Acceptance	0 days	Fri 17/04/26	Tue 28/04/26	Fri 17/04/26	Tue 28/04/26	0	\$0.00	\$0.00													
108		PIPP Pursat	25 days	Sat 06/06/26	Sat 06/06/26	Tue 30/06/26	Tue 30/06/26	0	\$0.00	\$0.00													
109		Client Inspection	10 days	Sat 06/06/26	Sat 02/05/26	Mon 15/06/26	Mon 11/05/26	0	\$0.00	\$0.00													
110		Defect Remediation	15 days	Tue 16/06/26	Tue 12/05/26	Tue 30/06/26	Tue 26/05/26	0	\$0.00	\$0.00													
111		Client Final Inspection Acceptance	0 days	Tue 30/06/26	Tue 26/05/26	Tue 30/06/26	Tue 26/05/26	0	\$0.00	\$0.00													
112		NPIA Siem Reap	25 days	Wed 08/04/26	Sat 06/06/26	Sat 02/05/26	Tue 30/06/26	0	\$0.00	\$0.00													
113		Client Inspection	10 days	Wed 08/04/26	Sat 02/05/26	Fri 17/04/26	Mon 11/05/26	0	\$0.00	\$0.00													
114		Defect Remediation	15 days	Sat 18/04/26	Tue 12/05/26	Sat 02/05/26	Tue 26/05/26	0	\$0.00	\$0.00													
115		Client Final Inspection Acceptance	0 days	Sat 02/05/26	Tue 26/05/26	Sat 02/05/26	Tue 26/05/26	0	\$0.00	\$0.00													
116		NIB Phnom Penh	25 days	Tue 24/03/26	Sat 06/06/26	Fri 17/04/26	Tue 30/06/26	0	\$0.00	\$0.00													
117		Client Inspection	10 days	Tue 24/03/26	Fri 05/06/26	Thu 02/04/26	Sun 14/06/26	0	\$0.00	\$0.00													
118		Defect Remediation	15 days	Fri 03/04/26	Mon 15/06/26	Fri 17/04/26	Mon 29/06/26	0	\$0.00	\$0.00													
119		Client Final Inspection Acceptance	0 days	Fri 17/04/26	Tue 30/06/26	Fri 17/04/26	Tue 30/06/26	0	\$0.00	\$0.00													
120		NTTI Phnom Penh	123 days	Tue 31/03/26	Tue 24/03/26	Fri 31/07/26	Fri 17/04/26	0	\$0.00	\$0.00													
121		Client Inspection Rooms 702-704-706	10 days	Tue 31/03/26	Tue 17/02/26	Thu 09/04/26	Thu 26/02/26	0	\$0.00	\$0.00													
122		Defect Remediation Rooms 702-704-706	15 days	Fri 10/04/26	Fri 27/02/26	Fri 24/04/26	Fri 13/03/26	0	\$0.00	\$0.00													
123		Client Final Inspection Acceptance Rooms 702-704-706	0 days	Fri 24/04/26	Fri 13/03/26	Fri 24/04/26	Fri 13/03/26	0	\$0.00	\$0.00													
124		Client Inspection Rooms 602-604	10 days	Sat 18/04/26	NA	Mon 27/04/26	NA	0	\$0.00	\$0.00													
125		Defect Remediations Rooms 602-604	15 days	Tue 28/04/26	NA	Tue 12/05/26	NA	0	\$0.00	\$0.00													
126		Client Final Inspection Acceptance Rooms 602-604	0 days	Tue 12/05/26	NA	Tue 12/05/26	NA	0	\$0.00	\$0.00													
127		Client Inspection Rooms 601-606-607-500-502	10 days	Tue 07/07/26	NA	Thu 16/07/26	NA	0	\$0.00	\$0.00													
128		Defect Remediations Rooms 601-606-607-500-502	15 days	Fri 17/07/26	NA	Fri 31/07/26	NA	0	\$0.00	\$0.00													
129		Client Final Inspection Acceptance Rooms 601-606-607-500-502	0 days	Fri 31/07/26	NA	Fri 31/07/26	NA	0	\$0.00	\$0.00													
130		PCCFPI Preah Sihanouk	25 days	Mon 23/03/26	Mon 23/03/26	Thu 16/04/26	Thu 16/04/26	0	\$0.00	\$0.00													
131		Client Inspection	10 days	Mon 23/03/26	Mon 16/02/26	Wed 01/04/26	Wed 25/02/26	0	\$0.00	\$0.00													
132		Defect Remediation	15 days	Thu 02/04/26	Thu 26/02/26	Thu 16/04/26	Thu 12/03/26	0	\$0.00	\$0.00													
133		Client Final Inspection Acceptance	0 days	Thu 16/04/26	Thu 12/03/26	Thu 16/04/26	Thu 12/03/26	0	\$0.00	\$0.00													
134		PIP Preah Sihanouk	25 days	Sun 08/03/26	Sun 08/03/26	Wed 01/04/26	Wed 01/04/26	0	\$0.00	\$0.00													
135		Client Inspection	10 days	Sun 08/03/26	Sun 01/02/26	Tue 17/03/26	Tue 10/02/26	0	\$0.00	\$0.00													
136		Defect Remediation	15 days	Wed 18/03/26	Wed 11/02/26	Wed 01/04/26	Wed 25/02/26	0	\$0.00	\$0.00													
137		Client Final Inspection Acceptance	0 days	Wed 01/04/26	Wed 25/02/26	Wed 01/04/26	Wed 25/02/26	0	\$0.00	\$0.00													
138		RPITSK Kampot	25 days	Tue 24/03/26	Tue 24/03/26	Fri 17/04/26	Fri 17/04/26	0	\$0.00	\$0.00													
139		Client Inspection	10 days	Tue 24/03/26	Tue 24/03/26	Thu 02/04/26	Thu 02/04/26	0	\$0.00	\$0.00													
140		Defect Remediation	15 days	Fri 03/04/26	Fri 03/04/26	Fri 17/04/26	Fri 17/04/26	0	\$0.00	\$0.00													
141		Client Final Inspection Acceptance	0 days	Fri 17/04/26	Fri 17/04/26	Fri 17/04/26	Fri 17/04/26	0	\$0.00	\$0.00													
142		NPIC Phnom Penh	25 days	Sat 02/05/26	Mon 25/05/26	Tue 26/05/26	Thu 18/06/26	0	\$0.00	\$0.00													
143		Client Inspection	10 days	Sat 02/05/26	Mon 20/04/26	Mon 11/05/26	Wed 29/04/26	0	\$0.00	\$0.00													
144		Defect Remediation	15 days	Tue 12/05/26	Thu 30/04/26	Tue 26/05/26	Thu 14/05/26	0	\$0.00	\$0.00													
145		Client Final Inspection Acceptance	0 days	Tue 26/05/26	Thu 14/05/26	Tue 26/05/26	Thu 14/05/26	0	\$0.00	\$0.00													
146		NPIT Kandal	25 days	Tue 21/04/26	Mon 25/05/26	Fri 15/05/26	Thu 18/06/26	0	\$0.00	\$0.00													
147		Client Inspection	10 days	Tue 21/04/26	Mon 20/04/26	Thu 30/04/26	Wed 29/04/26	0	\$0.00	\$0.00													
148		Defect Remediation	15 days	Fri 01/05/26	Thu 30/04/26	Fri 15/05/26	Thu 14/05/26	0	\$0.00	\$0.00													
149		Client Final Inspection Acceptance	0 days	Fri 15/05/26	Thu 14/05/26	Fri 15/05/26	Thu 14/05/26	0	\$0.00	\$0.00													
150		RPITST Takeo	25 days	Fri 08/05/26	Fri 08/05/26	Mon 01/06/26	Mon 01/06/26	0	\$0.00	\$0.00													
151		Client Inspection	10 days	Fri 08/05/26	Fri 03/04/26	Sun 17/05/26	Sun 12/04/26	0	\$0.00	\$0.00													
152		Defect Remediation	15 days	Mon 18/05/26	Mon 13/04/26	Mon 01/06/26	Mon 27/04/26	0	\$0.00	\$0.00													
153		Client Final Inspection Acceptance	0 days	Mon 01/06/26	Mon 27/04/26	Mon 01/06/26	Mon 27/04/26	0	\$0.00	\$0.00													
154		RPITSSR Svay Rieng	25 days	Mon 25/05/26	Mon 25/05/26	Thu 18/06/26	Thu 18/06/26	0	\$0.00	\$0.00													
155		Client Inspection	10 days	Mon 25/05/26	Mon 20/04/26	Wed 03/06/26	Wed 29/04/26	0	\$0.00	\$0.00													
156		Defect Remediation	15 days	Thu 04/06/26	Thu 30/04/26	Thu 18/06/26	Thu 14/05/26	0	\$0.00	\$0.00													
157		Client Final Inspection Acceptance	0 days	Thu 18/06/26	Thu 14/05/26	Thu 18/06/26	Thu 14/05/26	0	\$0.00	\$0.00													
158		OTHER	0 days</																				
